



**S**

**EASTERN REGION**

**29**

**TEMPORARY SPEED RESTRICTIONS  
PERMANENT WAY OPERATIONS  
SIGNAL ALTERATIONS  
APPENDIX INSTRUCTIONS, ETC.**

**AFFECTING EASTERN REGION TRAINMEN  
WORKING OVER SOUTHERN, LONDON MIDLAND,  
AND WESTERN REGIONS**

**SATURDAY 21 JULY  
TO  
FRIDAY 27 JULY 1979  
INCLUSIVE**

---

Trainmen must pay particular attention to works contained in this notice and keep a good look-out for hand signals, which will be exhibited at the various localities in accordance with the Rules and Regulations. Work at places other than those mentioned may be in progress of which it may not have been possible to give previous notice, and drivers must be on the look-out and be prepared to stop or run at reduced speed when and where hand signals may be exhibited.

---

## TEMPORARY SPEED RESTRICTIONS

Warning boards and indicators provided unless otherwise shown.

Portable magnets have additionally been provided for Temporary Speed Restrictions on all sections of line on the Western Region and London Midland Region which are equipped with A.W.S. as shown in Table Y, and which were not previously provided.

In the case of items marked \* the warning board (s) and indicators will be moved as the work progresses.

In the case of items marked † the warning board (s) will be lit by propane gas.

Where two speeds are shown for a restriction e.g.  $\frac{20}{40}$  the Rule Book Section T, clause 21.2 applies.

Location	Lines affected		Mileage at or between		Restriction m.p.h.	Remarks
			M. Chs. M. Chs.			
SOUTHERN REGION						
LATCHMERE JN. TO HITHER GREEN VIA NUNHEAD						
Factory Jn. and Longhedge	Down Ludgate	—	0 00	0 25	10	Trackwork.
Lewisham and Nunhead	—	Up	06 55	06 30	20	Condition of track.
LATCHMERE JN. TO GLOUCESTER ROAD JN. VIA STREATHAM COMMON						
Clapham Jn. and Wandsworth Common	Down Through	—	2 65	2 75	30	Condition of track.
Wandsworth Common and Clapham Jn.	—	Up Local	03 04	02 78	20	Earthworks. Commencing 08 00 Sunday 22 July
Streatham Common and Balham	—	Up Through	5 29	5 28	20	Earthworks. Until 15 00 Sunday 22 July.
BALHAM TO GATWICK AIRPORT VIA CRYSTAL PALACE						
Horley and Earlswood	—	Up Local	23 65	23 33	30	Trackwork. Commencing 20 30 Sunday 22 until 15 00 Thursday 26 July.
Earlswood and Horley	Down Local	—	23 33	23 65	20	Trackwork.

**SECTION A – TEMPORARY SPEED RESTRICTIONS – continued**

Location	Lines affected		Mileage at or between		Restriction m.p.h.	Remarks
			M. Chs.	M. Chs.		
SOUTHERN REGION – continued						
KEW EAST JN. TO EARLEY						
Ascot and Sunningdale	—	Up	27 50	27 40	20	Condition of track.
Winnersh and Wokingham	—	Up	63 40	63 20	15	Trackwork.
VIRGINIA WATER TO MILLBROOK						
Eastleigh and Shawford	—	Up Fast	71 25	71 10	40	Trackwork. Commencing 10 15 Friday 27 July.
Eastleigh East	—	Up Fast	73 32	73 15	<del>60</del> 90	Trackwork.
GUILDFORD TO NORTH CAMP						
Guildford and Wanborough	Down	—	31 75	32 25	20	Trackwork. Commencing 23 40 Friday 27 July.
Guildford and Wanborough	Down	—	32 25	32 60	20	Trackwork. Until 23 40 Friday 27 July.
Guildford and Wanborough	Down	—	32 25	32 60	40	Trackwork. Commencing 23 40 Friday 27 July.
Guildford and Wanborough	Down	—	32 60	33 15	40	Trackwork. Until 23 40 Friday 27 July.
Wanborough and Guildford	—	Up	33 40	32 40	<del>20</del> 40	Condition of embankment.
Farnborough North and North Camp	—	Up	52 60	52 05	40	Trackwork.

**LONDON MIDLAND REGION****BROAD STREET TO OLD KEW VIA WILLESDEN HIGH LEVEL**

†Hampstead Heath and Finchley Road	Down	—	1 60	2 37	20	Condition of track.
------------------------------------	------	---	------	------	----	---------------------

## SECTION A – TEMPORARY SPEED RESTRICTIONS – continued

Location	Lines affected		Mileage at or between		Restriction m.p.h.	Remarks
			M.	Chs.M. Chs.		
LONDON MIDLAND REGION – continued						
BROAD STREET TO OLD KEW VIA WILLESDEN HIGH LEVEL – continued						
†Finchley Road and West Hampstead	Down	—	2 37	2 65	10	Bridgework.
†Brondesbury and Finchley Road	—	Up	3 00	2 59	<u>10</u> 20	Bridgework No.35.
†Canonbury Jn. and Highbury	Down No.1	Up No.1	3 12	3 16	20	Condition of track.
†Brondesbury and Brondesbury Park	Down	—	3 54	3 79	30	Condition of track.
†Caledonian Road and Camden Road	Down No.2	—	4 15	4 62	20	Trackwork.

**CAMDEN ROAD JN. TO WOLVERTON VIA CAMDEN JN.**

Portable Magnets now in use for Temporary Speed Restrictions on this route.

†Harrow & Wealdstone and Bushey	Down Slow	—	14	55	15 22	30	Condition of track.
†Cheddington and Tring	—	Up Slow	33	15	32 60	20	Bridgework.
†Denbigh Hall Jn. and Bletchley	—	Up Slow	47	28	46 62	<u>20</u> 40	Condition of track.

**LATCHMERE JN. TO WILLESDEN WEST LONDON JN.**

†North Pole Jn. and Kensington North Main	—	Up	1	56	1 66	20	Trackwork.
---	---	----	---	----	------	----	------------

**UPPER HOLLOWAY TO CRICKLEWOOD (BRENT JN.)**

†*St. Pancras and West Hampstead	Down Slow	Up Slow	0	60	3 60	20	Trackwork and condition of track.
----------------------------------	-----------	---------	---	----	------	----	-----------------------------------

Warning Board situated on Down Slow line at St. Pancras Signal No.25.

The Warning Board situated on the Up Fast line at 4m. 41chs. applies also to trains travelling to the Up Slow line at West Hampstead.

The Warning Board situated on the Up Fast line at 2m. 23chs. applies only to trains travelling to the Up Slow line at Carlton Road Jn.

The Warning Board situated on the Up Goods line at 4m. 41chs. applies also to trains travelling to the Up Fast line at West Hampstead.

†Belsize Tunnel and West Hampstead	Down Fast	Up Fast	3	57	3 60	20	Condition of track.
------------------------------------	-----------	---------	---	----	------	----	---------------------

## SECTION A – TEMPORARY SPEED RESTRICTIONS – continued

Location	Lines affected		Mileage at or between		Restriction m.p.h.	Remarks
			M.	Chs. M.		
LONDON MIDLAND REGION – continued						
UPPER HOLLOWAY TO CRICKLEWOOD (BRENT JN.) – continued						
†Finchley Road and West Hampstead	Down Local	Up Local	3 57	3 60	20	Condition of track. Commencing 08 00 Saturday 21 July.

The Warning Board situated on the Down Fast line at 2m. 12chs. applies also to trains travelling to the Down Local line at Finchley Road. Commencing 08 00 Saturday 21 July.

The Warning Board situated on the Down Fast line at 4m. 24chs. applies only to trains travelling to the Down Local line at Cricklewood South Jn.

†Cricklewood South Jn. and Cricklewood Jn.	Down Local	Up Local	5	12	5 20	20	Platform work and trackwork.
--	------------	----------	---	----	------	----	------------------------------

## WESTERN REGION

## ACTON WELLS JN. TO SWINDON

The Warning Board located at 4m. 26chs. on the Up Relief line applies only to trains crossing to the Up Main line at Friars Jn.

†Slough (West) and Burnham	Down Main	—	19	53	20 00	20	Trackwork. Until 10 00 Sunday 22 July.
†Slough (West) and Burnham	Down Main	—	19	53	20 00	100	Trackwork. Commencing 10 00 Sunday 22 July.
†Taplow and Maidenhead (East)	Down Main	—	22	44	22 62	20	Trackwork. Commencing 10 00 Sunday 22 July.
Twyford (West) and Reading (East)	Down Relief	—	34	20	34 70	<u>30</u> 50	Condition of track. Miniature warning board in use.
†Didcot Station and Foxhall Jn.	Down Main	—	53	21	53 50	90	Condition of track. Commencing 10 00 Sunday 22 July.

## SECTION B

## TEMPORARY ENGINEERING WORKS

(For details of Signalling or Permanent Way Alterations see Section C)

Where any work involves fixing, removing or repairing of signals, or the protection of the running line during renewals, repairs and obstructions, Handsignalmen will be provided by the Engineer to act in accordance with the Rules and Regulations.

Materials may be lying about and disconnections may be made as required.

Unless otherwise shown, work will be carried out as traffic permits.

Although the S notice commences on Saturday of each week, items may be included which are shown to commence on the previous night, and were not available for inclusion in the previous notice.

All concerned must therefore not assume that items shown to commence before the operative date of each notice will have been published in the previous one, and on Friday nights must refer to both the current and following notice.

At or between	Lines affected	Remarks
<b>SOUTHERN REGION</b>		
<b>ALL LINES</b>		
<b>UNTIL FURTHER NOTICE</b>		
All Signal Boxes	All	00 05 to 17 00 Sun. 00 05 to 05 00 Weekdays. 10 00 to 16 00 Mon to Fri. S & T work.
<b>LATCHMERE JN. TO HITHER GREEN VIA NUNHEAD</b>		
<b>SATURDAY 21 JULY</b>		
Parks Bridge Jn. and Hither Green	Down and Up Fast <b>BLOCKED</b>	00 30 to 05 00. Trackwork between 6m. 35chs. and 7m. 25chs. <b>Trains to travel on Slow lines.</b>
<b>SUNDAY 22 JULY</b>		
Battersea Pier Jn. and Brixton Jn.	All <b>BLOCKED</b>	00 50 to 05 15. Trackwork between 0m. 70chs. and 3m. 10chs.
Stewarts Lane and Factory Jn.	Down and Up Main Up Reception Loco Sheds, Yard Roads Electric Roads <b>BLOCKED</b>	00 30 to 05 20. Demolition work between 1½ and 1¾ m.p.
Factory Jn.	Down and Up Ludgate Down and Up Stewarts Lane <b>BLOCKED</b>	00 50 to 05 20. Trackwork.
Factory Jn. and Longhedge Jn.	Down and Up Ludgate <b>BLOCKED</b>	00 30 to 05 15. Trackwork between 0m. 30chs. and 1m. 66chs.
Nunhead and Lewisham	Down and Up <b>BLOCKED</b>	00 10 to 06 10. Unloading between 6m. 10chs. and 7m. 70chs.

**SECTION B – TEMPORARY ENGINEERING WORKS – continued**

At or between	Lines affected	Remarks
<b>SOUTHERN REGION – continued</b>		
<b>BRIXTON TO WEST NORWOOD JN.</b>		
<b>UNTIL FURTHER NOTICE</b> Herne Hill	All	Platform work between 3m 71chs and 4m 1chs.
<b>SUNDAY 22 JULY</b> Herne Hill and Tulse Hill	Down and Up Branch <b>BLOCKED</b>	00 40 to 06 30. Trackwork between 4m. 10chs. and 4m. 63chs.
<b>TUESDAY 24 to FRIDAY 27 JULY</b> Herne Hill	Down and Up Main <b>BLOCKED</b>	00 50 to 04 20 daily. Trackwork between 3m. 70chs. and 4m. 6chs. <b>Trains to travel on Loop lines.</b>
<b>LATCHMERE JN. TO GLOUCESTER ROAD JN. VIA STREATHAM COMMON</b>		
<b>UNTIL FURTHER NOTICE</b> Clapham Jn. 'B'	Down and Up West London	07 30 to 17 00 Mon to Sat. Building work.
Selhurst	All	Installation of oil pipes.
<b>FRIDAY 20 to SATURDAY 21 JULY</b> Streatham Common and Selhurst	Down Local <b>BLOCKED</b> Up Local <b>BLOCKED</b>	00 10 to 04 50 ) Trackwork between ) 6½m.p. and 9m. 42chs. 23 55 Fri to 04 50 Sat ) <b>Trains to travel on</b> ) <b>Through lines, trains</b> <b>cannot pass to or from Streatham Spurs, Selhurst</b> <b>Spurs, Norwood Fork Spurs or Selhurst Depot.</b>
<b>SATURDAY 21 JULY</b> Battersea Park and Clapham Jn.	Down and Up Local <b>BLOCKED</b>	00 05 to 05 00. Bridgework and trackwork between 1m. 35chs. and 2m. 35chs. <b>Trains to travel on</b> <b>Through lines.</b>
Clapham Jn. and Balham	Down and Up Local <b>BLOCKED</b>	00 05 to 05 00. Trackwork between 3m.p. and 4m. 50chs. <b>Trains to travel on Through lines.</b>
Gloucester Road Jn. and East Croydon	Reversible/ Platform 6 <b>BLOCKED</b>	00 30 to 05 00. Trackwork between 9¼m.p. and 10m. 3chs. <b>Trains to travel on alternative lines.</b>
<b>SATURDAY 21 to SUNDAY 22 JULY</b>		
Clapham Jn. and Balham	Down and Up Local <b>BLOCKED</b>	23 55 Sat to 08 50 Sun. Trackwork between 3m.p. and 4m. 50chs. <b>Trains to travel on Through lines.</b> Crane in use.
<b>SUNDAY 22 JULY</b> Battersea Park Jn. and Clapham Jn.	Down and Up Local <b>BLOCKED</b>	00 05 to 23 30. Bridgework between 1¼m.p. and 2m. 30chs. <b>Trains to travel on Through lines.</b>
Clapham Jn. and Balham	Down Through <b>Between Trains</b>	00 05 to 06 00. In connection with trackwork.
Balham and Norbury	Down and Up Through <b>BLOCKED</b>	00 15 to 06 30. Trackwork between 5m. 30chs. and 18m. 10chs. <b>Trains to travel on Local lines;</b> <b>trains cannot pass to or from Through Spurs.</b>

**SECTION B – TEMPORARY ENGINEERING WORKS – continued**

At or between	Lines affected	Remarks
<b>SOUTHERN REGION – continued</b>		
<b>LATCHMERE JN. TO GLOUCESTER ROAD JN. VIA STREATHAM COMMON – continued</b>		
<b>SUNDAY 22 JULY – continued</b>		
Windmill Bridge Jn. and East Croydon	Reversible/ Platform 6 <b>BLOCKED</b>	00 20 to 06 55. Trackwork between 9m. 75chs. and 10m. 36chs. <b>Trains to travel on alternative lines.</b>
East Croydon	All	00 30 to 08 00. S & T work.
<b>TUESDAY 24 JULY</b>		
Balham and Norbury	Down and Up Local <b>BLOCKED</b>	00 50 to 04 30. Unloading between 5m. 30chs. and 8m. 10chs. <b>Trains to travel on Through lines, trains cannot pass to or from Local Spurs or Streatham Spurs.</b>
<b>TUESDAY 24 to FRIDAY 27 JULY</b>		
Clapham Jn. and Balham	Down and Up Local <b>BLOCKED</b>	00 05 to 05 00 daily. Trackwork between 3 m.p. and 4m. 50chs. <b>Trains to travel on Through lines.</b>
<b>CLAPHAM JN. C TO LATCHMERE JN.</b>		
<b>UNTIL FURTHER NOTICE</b>		
Clapham Jn. 'C'	All	00 05 to 07 20 Sun, 00 05 to 05 20 Weekdays. S & T work.
West London Jn. and Clapham Jn. 'A'	All	10 00 to 15 00 Mon to Fri, 00 05 to 07 30 and 08 00 to 17 00 Sun. S & T work.
Stewarts Lane/FactoryJn. and Pouparts Jn./Clapham Jn./Latchmere Jn.	All	Bridgeworks.
<b>BALHAM TO GATWICK AIRPORT VIA CRYSTAL PALACE</b>		
<b>UNTIL FURTHER NOTICE</b>		
Balham	All	00 05 to 05 00 Sat. S & T. work.
Coulsdon North	All	00 01 to 17 00 Sun. S & T work.
Coulsdon North and Earlswood/Coulsdon South and Merstham	All	Falling chalk between 16¼ and 17¼m.p. and between 18¼ and 19m.p.
Earlswood	All	00 05 to 17 00 Sun. S & T work.
Earlswood and Gatwick Airport	All, including area between Station and Up Carriage Sidings	Bridgeworks and buildingwork affecting walkway. Machines in use.
Gatwick Airport	Platform 6/Down Platform Loop <b>Between Trains</b>	22 00 to 06 30 also 08 00 to 18 00. Buildingwork between 26½m.p. and 26m. 55chs. <b>Commencing Saturday 21 July.</b>



## SECTION B – TEMPORARY ENGINEERING WORKS – continued

At or between	Lines affected	Remarks
<b>SOUTHERN REGION – continued</b>		
<b>BALHAM TO GATWICK AIRPORT VIA CRYSTAL PALACE – continued</b>		
<b>FRIDAY 20 to SATURDAY 21 JULY</b>		
Gatwick Airport	Platform 1/ Up Platform Loop <b>BLOCKED</b>	23 25 Fri to 06 00 Sat ) Building work between 26½ m.p. and 26m
	Platform 2/ Up Local <b>BLOCKED</b>	23 55 Fri to 05 30 Sat ) 55chs. Trains to travel on alternative platform lines.
	Platform 3/ Down Local <b>BLOCKED</b>	00 40 to 05 30 Sat )
	Platform 6/Down Platform Loop <b>BLOCKED</b>	23 00 Fri to 07 30 Sat )
<b>SATURDAY 21 JULY</b>		
East Croydon	All	00 30 to 07 00. S and T work.
East Croydon and S. Croydon	Down and Up Local <b>BLOCKED</b>	00 30 to 06 00. Bridgework between 10¼ and 11½m.p. Trains to travel on Through lines.
Purley and Redhill 'A'	Down Through/ Down Redhill <b>BLOCKED</b>	01 20 to 05 00 ) Trackwork between 14¼ and 22m.p. Trains to travel on Local lines
	Up Through/ Up Redhill <b>BLOCKED</b>	00 35 to 04 35 ) and via Quarry. On track machines in use.
Earlswood and Gatwick Airport	Down and Up Local <b>BLOCKED</b>	00 25 to 05 10. Trackwork between 21m. 35chs. and 26½m.p. Trains to travel on Through lines.
<b>SATURDAY 21 to SUNDAY 22 JULY</b>		
Earlswood and Horley	Down Local <b>BLOCKED</b>	00 30 to 20 30 ) Trackwork between 21m. 35chs. and 26m.p.
	Up Local <b>BLOCKED</b>	23 35 Sat to 20 30 Sun ) Trains to travel on Through lines. On track machine in use.
Gatwick Airport	Platform 1/Up Platform Loop <b>BLOCKED</b>	23 55 Sat to 18 00 Sun. Building work between 26½m.p. and 26m. 55chs.
Gatwick Airport	Platform 2/Up Local <b>BLOCKED</b>	23 25 Sat to 07 00 Sun ) Building work between 26½m.p. and 26m.
	Platform 3/Down Local <b>BLOCKED</b>	00 40 to 07 00 ) 55chs. Trains to travel on alternative Platform lines.
	Platform 6/Down Platform Loop <b>BLOCKED</b>	23 00 Sat to 08 00 Sun )
<b>SUNDAY 22 JULY</b>		
East Croydon and Purley	Down and Up Through and Reversible <b>BLOCKED</b>	00 20 to 06 55. Bridgework between 10½ and 13¾m.p. Trains to travel on Local lines.
Purley	All	08 00 to 17 00. S and T work.
Earlswood and Horley	Down and Up Local <b>BLOCKED</b>	00 25 to 05 10. Trackwork between 21m. 35chs. and 26m.p. Trains to travel on Through lines. On track machine in use.

## SECTION B – TEMPORARY ENGINEERING WORKS – continued

At or between	Lines affected	Remarks	
SOUTHERN REGION – continued			
BALHAM TO GATWICK AIRPORT VIA CRYSTAL PALACE – continued			
MONDAY 23 to WEDNESDAY 25 JULY			
Gatwick Airport	Platform 1/ Up Platform Loop	23 25 Mon and Tue to 05 25 Tue and Wed	) Building work between 26½ m.p. and 26m. 55chs. <b>Trains to travel on alternative platform lines.</b>
	<b>BLOCKED</b>		
	Platform 2/ Up Local	23 55 Mon and Tue to 05 30 Tue and Wed	
	<b>BLOCKED</b>		
	Platform 3/ Down Local	00 40 to 06 20 Tue and Wed	
	<b>BLOCKED</b>		
TUESDAY 24 and WEDNESDAY 25 JULY			
East Croydon and Purley	Platform 5/ Down Through	00 20 to 05 00 daily	) Trackwork and building work between 10¼ and 13½ m.p. <b>Trains to travel on Local lines. On track machines in use.</b>
	<b>BLOCKED</b>		
	Platform 4/ Up Through	00 40 to 04 40 daily	
	<b>BLOCKED</b>		
WEDNESDAY 25 to FRIDAY 27 JULY			
Gatwick Airport	Platform 3/ Down Local	23 45 Wed and Thu to 05 15 Thu and Fri	) Building work between 26½ m.p. and 26m. 55chs. <b>Trains to travel on alternative platform lines.</b> Crane in use.
	<b>BLOCKED</b>		
	Platform 4/ Up Through	23 05 Wed and Thu to 05 40 Thu and Fri.	
	<b>BLOCKED</b>		
	Platform 5/ Down Through	23 50 Wed and Thu to 07 30 Thu and Fri.	
	<b>BLOCKED</b>		
	Platform 6/Down Platform Loop	23 00 Wed and Thu to 07 30 Thu and Fri	
	<b>BLOCKED</b>		
THURSDAY 26 JULY			
Redhill 'A' and Redhill 'B'	Down Local and Down Main	01 35 to 03 45. Trackwork between 22m. 15chs. and 22½ m.p. Crane in use.	
	<b>BLOCKED</b>		
THURSDAY 26 and FRIDAY 27 JULY			
South Croydon and Coulsdon North	Down Through	00 20 to 05 00 daily	) Trackwork between 11½ and 14¾ m.p. <b>Trains to travel on Local lines. On track machine in use.</b>
	<b>BLOCKED</b>		
	Up Through	00 40 to 04 40 daily	
	<b>BLOCKED</b>		
KEW EAST JN. TO EARLEY			
UNTIL FURTHER NOTICE			
Feltham	All	00 05 to 05 20 Sat. 00 05 to 07 20 and 09 00 to 16 30 Sun. S & T work.	
Feltham	All	10 00 to 16 00 and 20 00 to 05 00 daily. S & T work.	
Feltham West Level Crossing	All	09 30 to 15 30. S & T work.	

**SECTION B – TEMPORARY ENGINEERING WORKS – continued**

At or between	Lines affected	Remarks
<b>SOUTHERN REGION – continued</b>		
<b>BALHAM TO GATWICK AIRPORT VIA CRYSTAL PALACE – continued</b>		
<b>UNTIL FURTHER NOTICE – continued</b>		
Thorpe Lane Level Crossing	All	09 30 to 15 30. S & T work.
Egham Level Crossing	All	09 30 to 15 30. S & T work.
<b>SATURDAY 21 JULY</b>		
Virginia Water and Ascot	Down and Up <b>BLOCKED</b>	00 05 to 05 55. Trackwork between 23¼ and 28 m.p.
Ascot	Down Platform Loop <b>BLOCKED</b>	00 20 to 06 10. Trackwork between 29 and 40½m.p.
<b>SUNDAY 22 JULY</b>		
Ascot and Wokingham	Down and Up, Down and Up Frimley <b>BLOCKED</b>	00 10 to 05 55. Trackwork between 27¼ and 35/29¼m.p.
Feltham and Ashford	Down and Up <b>BLOCKED</b>	01 10 to 06 45. Trackwork between 14¼ and 15½m.p.
Staines and Egham	Down and Up <b>BLOCKED</b>	00 25 to 06 30. Trackwork between 19m. 10chs. and 20m.p. Crane in use.
Sunningdale and Wokingham/Bagshot	Down and Up, Down and Up Frimley <b>BLOCKED</b>	00 10 to 07 45. Trackwork between 27¼ and 35/29¼m.p.
Wokingham and Earley	Down and Up <b>BLOCKED</b>	00 20 to 07 45. Trackwork between 36/61¼ and 64½m.p.
<b>MONDAY 23 to FRIDAY 27 JULY</b>		
New Kew Jn. and Hounslow Jn.	Down and Up <b>BLOCKED</b> Up <b>BLOCKED</b>	00 20 to 05 10 daily Tue to Fri 23 30 Mon to Thu to 05 00 Tue to Fri ) Trackwork between 9m. ) 46chs. and 14 m.p. On ) track machines in use.
<b>TUESDAY 24 to FRIDAY 27 JULY</b>		
Virginia Water and Ascot	Down and Up <b>BLOCKED</b>	00 05 to 05 55 daily. Loading materials between 23¼ and 28 m.p.
<b>VIRGINIA WATER TO MILLBROOK</b>		
<b>UNTIL FURTHER NOTICE</b>		
Virginia Water and Chertsey	Down and Up	Bridgework between 23¼m.p. and 23m. 35chs.
Chertsey Level Crossing	All	09 30 to 15 30. S. & T. work.
Woking	All	00 05 to 07 00 Tue to Sat. S. & T. work.
Pirbright Jn. and Farnborough	Down Slow	07 30 to 18 00 Mon to Sat Earthworks at 30m. 27chs. Off track machines in use.

**SECTION B – TEMPORARY ENGINEERING WORKS – continued**

At or between	Lines affected	Remarks
<b>SOUTHERN REGION – continued</b>		
<b>VIRGINIA WATER TO MILLBROOK – continued</b>		
<b>UNTIL FURTHER NOTICE – continued</b>		
Hook and Basingstoke	Down and Up Fast, Down and Up Slow	05 00 to 16 30 Mon to Fri. Bridgework No.133 between 47m. 30chs. and 47m. 32chs. Scaffolding in use.
St. Denys/ Northam Jn.	All	08 00 to 16 00. S & T work. <b>Commencing 08 00 Sunday 22 July.</b>
Southampton/Millbrook	All	08 00 to 16 00. S and T work. <b>Commencing Sunday 22 July.</b>
Southampton and Millbrook	Down and Up Local	07 30 to 20 00 Mon to Sat. Bridgework at 79m 75chs. Cranes and off track machines in use.
Millbrook	Up Local	08 00 to 17 00 Mon to Fri. S and T work at 80m 11chs.
<b>FRIDAY 20 to SATURDAY 21 JULY</b>		
Hampton Court Jn. and Woking	Down and Up Fast <b>BLOCKED</b>	23 30 Fri to 06 10 Sat. Trackwork between 13½m.p. and 24m. 5chs. <b>Trains to travel on Slow lines.</b>
Walton-on-Thames and Byfleet & New Haw	Down Slow <b>Between Trains</b>	23 30 Fri to 06 00 Sat. Trackwork between 17¼m.p. and 19m. 34chs.
Woking and Brookwood	Down Fast <b>BLOCKED</b> Down Slow <b>Between Trains</b>	23 30 Fri to 06 00 Sat. Trackwork between 27m. 33chs. and 28m. 10chs. <b>Trains to travel on Slow line.</b>
Farnborough and Winchfield	Down and Up Fast <b>BLOCKED</b>	23 30 Fri to 06 30 Sat. Loading between 32m. 70chs. and 39½m.p. <b>Trains to travel on Slow lines.</b>
<b>SATURDAY 21 JULY</b>		
Steventon and Basingstoke	Up Southampton/ Up Slow <b>BLOCKED</b>	00 01 to 07 00. Trackwork between 52m. 54chs. and 48m. 50chs.
<b>SATURDAY 21 to SUNDAY 22 JULY</b>		
Hampton Court Jn. and Woking	Down and Up Fast <b>BLOCKED</b>	23 30 Sat to 07 00 Sun. Trackwork between 13½m.p. and 24m. 5chs. <b>Trains to travel on Slow lines.</b>
Wallers Ash and Winchester	Down <b>BLOCKED</b> Up <b>BLOCKED</b>	01 00 to 07 00 ) Trackwork between 23 55 Sat to 06 55 Sun ) 64m. 24chs. and 66m. 45chs. <b>Possession given up to pass 20 20 ex Stirling on the Down.</b>
Shawford and Eastleigh East	Down and Up Fast <b>BLOCKED</b> Up Slow <b>BLOCKED</b>	23 40 Sat to 06 25 Sun ) Trackwork between 23 40 Sat to 06 25 Sun ) 71m. 23chs. and 73m. 25chs. <b>Possession given up to pass 01 38 and 01 44 ex Eastleigh. Down trains to travel on Slow line. 06 25 to 07 45 Up trains to travel on Slow line.</b>

**SECTION B – TEMPORARY ENGINEERING WORKS – continued.**

At or between	Lines Affected	Remarks
<b>SOUTHERN REGION – continued</b>		
<b>VIRGINIA WATER TO MILLBROOK – continued</b>		
<b>SATURDAY 21 to SUNDAY 22 JULY – continued</b>		
Northam Jn. and Southampton	Down <b>BLOCKED</b> Up <b>BLOCKED</b>	23 40 Sat to 06 30 Sun ) Tunnelwork between 00 40 to 06 30 Sun ) 78m. 25chs. and 79m.p. Possession given up to pass 23 36 ex Portsmouth Hbr. on the Down and 03 05 ex Eastleigh D.E.M.U. depot on the Up.
Millbrook and Redbridge	Down and Up Main <b>BLOCKED</b>	23 40 Sat to 06 25 Sun ) Earthwork between 80½ and 80¾m.p. Possession given up to pass 20 20 ex Stirling on the Down.
Millbrook F.L.T.	Arrival and Departure Roads <b>BLOCKED</b>	00 30 to 11 00 Sun )
<b>SUNDAY 22 JULY</b> Farnborough and Woking	Up Slow <b>BLOCKED</b> Up Fast Between Trains	00 05 to 07 15. Trackwork between 25¼ and 32½m.p. Trains to travel on Fast line. Possession given up to pass 05 56 ex Basingstoke on the Fast line.
<b>MONDAY 23 to TUESDAY 24 JULY</b>		
Woking (London End) and Woking	Down Fast <b>BLOCKED</b>	) 23 55 Mon to 06 00 Tue. Trackwork between 24¼m.p. and 24m. 55chs. Trains to travel on Slow lines. )
Woking Jn. and Woking (London End)	Up Fast <b>BLOCKED</b>	) )
<b>TUESDAY 24 to WEDNESDAY 25 JULY</b>		
Woking Jn. and Woking (London End)	Up Fast <b>BLOCKED</b> Up Slow Between Trains	23 30 Tue to 06 00 Wed. Trackwork between 24¼ and 24m. 55chs. Trains to travel on Slow line.
<b>WEDNESDAY 25 to THURSDAY 26 JULY</b>		
Woking Jn. and Woking (London End)	Up Fast <b>BLOCKED</b> Up Slow Between Trains	23 30 Wed to 06 00 Thu. Trackwork between 24m. 36chs. and 24m. 18chs. Trains to travel on Slow line.
<b>THURSDAY 26 to FRIDAY 27 JULY</b>		
Woking and Brookwood	Down and Up Fast <b>BLOCKED</b>	23 30 Thu to 06 00 Fri. Trackwork between 24m. 69chs. and 27m. 30chs. Trains to travel on Slow lines.
<b>GUILDFORD TO NORTH CAMP</b>		
<b>UNTIL FURTHER NOTICE:</b>		
Ash and Wokingham	All	S and T work. Commencing 10 00 Monday 23 July.

**SECTION B – TEMPORARY ENGINEERING WORKS – continued**

At or between	Lines affected	Remarks
<b>SOUTHERN REGION – continued</b>		
<b>GUILDFORD TO NORTH CAMP – continued</b>		
<b>FRIDAY 20 to SATURDAY 21 JULY</b>		
Guildford and Ash	Down <b>BLOCKED</b> Up Between Trains	23 40 Fri to 04 30 Sat. Trackwork between 30¾m.p. and 34m. 22chs. Crane in use.
<b>SUNDAY 22 JULY</b>		
Guildford and Ash	Down and Up <b>BLOCKED</b>	00 30 to 18 15. Trackwork. Crane in use.
<b>MONDAY 23 to FRIDAY 27 JULY</b>		
Guildford and Ash	Down <b>BLOCKED</b> Up Between Trains	23 40 Mon to Thu to 04 30 Tue to Fri. Trackwork between 30¾m.p. and 34m. 22chs. Crane in use.
<b>SOUTHCOTE JN. TO BASINGSTOKE</b>		
<b>UNTIL FURTHER NOTICE</b>		
Southcote Jn. and Basingstoke	All	08 00 to 16 30 Mon to Fri and 08 00 to 20 00 Sat and Sun. S & T work.
<b>LONDON MIDLAND REGION</b>		
<b>BROAD STREET TO OLD KEW JN. (VIA WILLESDEN H.L.)</b>		
<b>SUNDAY 22 JULY</b>		
Broad St. and Dalston Western Jn.	Down and Up <b>BLOCKED</b>	00 01 to 08 15. Trackwork between 0 and 0½m.p.
Dalston Western Jn. and Camden Rd Jn.	Down and Up No.2's <b>BLOCKED</b>	00 01 to 08 30. Bridgework and buildingwork between 2¾ and 5m.p.
Camden Road Jn. and Gospel Oak	Down and Up <b>BLOCKED</b>	00 01 to 08 00. S and T work between 0 and 1m.p. Possession given up to pass 5Z88 E.C.S. Willesden to Gospel Oak.
<b>CAMDEN ROAD JN. TO WOLVERTON VIA CAMDEN JN.</b>		
<b>UNTIL FURTHER NOTICE</b>		
Watford Carriage Shed	Siding No.2 <b>BLOCKED</b>	Building work and trackwork. Machines in use.
Hemel Hempstead	Up Goods <b>BLOCKED</b>	08 00 to 17 00. Building work between 24 and 24½m.p.
<b>SATURDAY 21 to SUNDAY 22 JULY</b>		
Watford Jn. and Hemel Hempstead	Down and Up Fast <b>BLOCKED</b>	23 00 Sat to 07 00 Sun. Overhead line work between 24 and 24½m.p. <b>Trains to travel over Slow lines.</b>
Bletchley and Hanslope	Down and Up Fast <b>BLOCKED</b>	23 00 Sat to 16 00 Sun. Overhead line work between 49 and 50¾m.p. <b>Trains to travel over Slow lines.</b> Crane in use.

## SECTION B – TEMPORARY ENGINEERING WORKS – continued

At or between	Lines affected	Remarks
<b>LONDON MIDLAND REGION – continued</b>		
<b>CAMDEN ROAD JN. TO WOLVERTON VIA CAMDEN JN. – continued</b>		
<b>SUNDAY 22 JULY</b> Camden Road Jn. and Camden Jn.	Down and Up <b>BLOCKED</b>	00 01 to 12 00. S and T work between 5¼ and 5½m.p. Possession given up to pass 0E15 and 6E15 and 5Z88.
Willesden and Wembley Central	Down and Up Fast <b>BLOCKED</b>	00 01 to 06 00. Trackwork between 6¼ and 5¾m.p. Trains to travel over Slow lines.
Willesden and Wembley Central	Down and Up Fast <b>BLOCKED</b>	06 00 to 15 30. Trackwork between 6¼ and 6½m.p. Trains to travel over Slow lines.
Willesden and Wembley Central	Down and Up Low Level Goods <b>BLOCKED</b> "G" Sidings 1 to 3 <b>BLOCKED</b> (to electric trains)	08 00 to 17 00. Painting Bridgework No.29 between 6¼ and 6½m.p.
Willesden and Harrow & Wealdstone	Down and Up Fast <b>BLOCKED</b>	00 01 to 15 30. Bridgework and trackwork between 6¼ and 8¼m.p. Trains to travel over Slow lines. Ladders in use.
Willesden and Harrow & Wealdstone	Down and Up Fast <b>BLOCKED</b>	00 01 to 08 00. L.T.E. bridgework 37A at 10m.p. Trains to travel over Slow lines. Ladders in use.
Harrow & Wealdstone and Hemel Hempstead	Down and Up Slow <b>BLOCKED</b>	07 30 to 16 00. Overhead line work between 16 and 20½m.p. Trains to travel over Fast lines. Ladders in use.
Harrow & Wealdstone and Hemel Hempstead	Down and Up Slow <b>BLOCKED</b>	07 30 to 16 00. Trackwork between 14½ and 12m.p. Trains to travel on Fast lines. On track machines in use.
Watford Jn. and Hemel Hempstead	Down Slow <b>BLOCKED</b> (to electric trains)	01 45 to 04 45. In connection with overhead line work.
Hemel Hempstead	All	00 01 to 08 30. S and T work.
Tring and Ledburn Jn.	Down and Up Slow <b>BLOCKED</b>	00 01 to 16 00. Bridgework between 34 and 33 m.p. Trains to travel over Fast lines. Off track machines in use.
Tring and Ledburn Jn.	Down and Up Slow <b>BLOCKED</b>	06 00 to 16 00. Trackwork between 36¼ and 37m.p. Trains to travel on Fast lines.
Bletchley and Hanslope	Down and Up Fast <b>BLOCKED</b>	06 00 to 16 00. Trackwork and bridgework between 52¼ and 56 m.p. Trains to travel on Slow lines.
Bletchley and Hanslope	Down and Up Fast <b>BLOCKED</b>	07 30 to 16 00. Bridgework between 48 and 50¼m.p. Trains to travel on Slow lines.
Bletchley and Hanslope	Down and Up Fast <b>BLOCKED</b>	06 00 to 16 00. Overhead line work between 47½ and 48½m.p. Trains to travel over Slow lines. Ladders in use.

**SECTION B – TEMPORARY ENGINEERING WORKS – continued**

At or between	Lines affected	Remarks
<b>LONDON MIDLAND REGION – continued</b>		
<b>CAMDEN ROAD JN. TO WOLVERTON VIA CAMDEN JN. – continued</b>		
<b>SUNDAY 22 JULY – continued</b>		
Denbigh Hall	All	08 30 to 16 00. S and T work.
Denbigh Hall and Wolverton	Down and Up Slow <b>BLOCKED</b> (to electric trains)	02 15 to 14 30. In connection with overhead line work between 49 and 50¼m.p. Cranes in use.
Denbigh Hall and Wolverton	Down and Up Slow	02 15 to 14 30. In connection with overhead line work between 49 and 50¼m.p. Cranes in use.
<b>MONDAY 23 JULY</b>		
Bletchley Lambs Sdgs.	Down Fast	08 00 to 16 00. Signalling work. (See Section 'C').
Bletchley and Hanslope	Down and Up Fast <b>BLOCKED</b>	00 40 to 06 00. Unloading rails between 51¼ and 52¼m.p. <b>Trains to travel over Slow lines.</b>
<b>TUESDAY 24 to FRIDAY 27 JULY</b>		
Denbigh Hall and Hanslope	Down and Up Slow <b>BLOCKED</b>	00 30 to 06 00 daily. Speno rail grinding between 48¼ and 56¼m.p. <b>Trains to travel over Fast lines.</b> <b>Note:—Sparks will be emitted during grinding operations.</b> On track machine in use.
<b>WEDNESDAY 25 JULY</b>		
Wembley Central and Harrow & Wealdstone	Down and Up Slow <b>BLOCKED</b>	02 00 to 04 00. Unloading materials at 10¾m.p. <b>Trains to travel over Fast lines.</b>
<b>THURSDAY 26 JULY</b>		
Willesden and Wembley Central	Down and Up Fast <b>BLOCKED</b>	02 00 to 04 00. Unloading materials between 7¼ and 7¾m.p. <b>Trains to travel over Slow lines.</b>
<b>UPPER HOLLOWAY TO CRICKLEWOOD (BRENT JN.)</b>		
<b>UNTIL FURTHER NOTICE</b>		
St. Pancras and West Hampstead	All	Bridgework at 3¾ m.p. Off track machines in use.
<b>SATURDAY 21 JULY</b>		
Cricklewood Jn. and Elstree	Down Fast <b>BLOCKED</b>	07 00 to 12 00. Unloading stone between 10¼ and 10¾ m.p. <b>Trains to travel on Local/Slow line.</b>
<b>SUNDAY 22 JULY</b>		
St. Pancras and Cricklewood Jn.	Down and Up Fast <b>BLOCKED</b>	06 00 to 16 00. Trackwork between ¼ and 4¼ m.p. <b>Trains to travel on Slow lines. Access NOT available to Cambridge Street DD.</b> Crane in use.
West Hampstead and Cricklewood South Jn.	All	00 15 to 10 00. In connection with bridgework between 4¼ and 4½m.p. Crane in use.
Cricklewood South Jn. and Hendon	Down and Up Local and Down and Up Goods	06 00 to 15 00. In connection with S & T work between 5½ and 6½m.p.



**SECTION B – TEMPORARY ENGINEERING WORKS – continued**

At or between	Lines affected	Remarks
<b>LONDON MIDLAND REGION – continued</b>		
<b>UPPER HOLLOWAY TO CRICKLEWOOD (BRENT JN.) – continued</b>		
<b>SUNDAY 22 to MONDAY 23 JULY</b>		
St. Pancras and Cricklewood South Jn.	Down Fast <b>BLOCKED</b>	) 00 45 Sun to 05 30 Mon. Earthwork, trackwork and ) overhead line work in Belsize tunnel between 0¾ ) and 3½ m.p. <b>Trains to travel on Slow lines.</b> ) <b>Crossing facilities available Up Fast to Up Slow</b> ) <b>at West Hampstead.</b> On track machines in use.
West Hampstead and St. Pancras	Up Fast <b>BLOCKED</b>	
Cricklewood South Jn. and St. Albans	Down and Up Fast <b>BLOCKED</b>	
		00 15 Sun to 06 00 Mon. S and T work between 5½ and 6½ m.p. <b>Trains to travel on Slow/Local</b> <b>lines.</b> Crane in use.
<b>MONDAY 23 JULY</b>		
Cricklewood South Jn. and Finchley Road	Up Local <b>BLOCKED</b>	11 00 to 16 00. Earthworks between 5 and 3¾ m.p. <b>Trains to travel on Fast line.</b>
<b>MONDAY 23 to FRIDAY 27 JULY</b>		
Cricklewood South Jn. and St. Albans	Down and Up Fast <b>BLOCKED</b>	22 00 Mon to Thu to 05 40 Tue to Fri. Trackwork between 5½ and 18 m.p. <b>Trains to travel on Local/</b> <b>Slow lines.</b> On track machines in use.
Cricklewood South and St. Albans	Down and Up Fast <b>BLOCKED</b>	22 00 Mon to Thu to 05 40 Tue to Fri. Trackwork between 7 and 19½ m.p. <b>Trains to travel on Local/</b> <b>Slow lines.</b>
<b>WEDNESDAY 25 and THURSDAY 26 JULY</b>		
Cricklewood South Jn. and St. Albans	Down and Up Fast <b>BLOCKED</b>	01 00 to 02 00 daily. Trackwork between 13½ and 15 m.p. <b>Trains to travel on Local/Slow lines.</b>

**WESTERN REGION****ACTON WELLS JN. TO SWINDON****UNTIL FURTHER NOTICE**

Acton Wells Jn. and Hayes	All	Signalling work.
Subway Jn. and Slough	All	S & T work.
Hanwell	Down and Up Relief and Up Main	Building work between 7¼ and 7½ m.p.
At Hayes	All	07 30 to 17 00. Bridgework at 10m. 77chs.
Reading (West Main)	Pilot Line and Up Reception Line	08 00 to 16 00. Earthworks at 36m. 33chs.
Goring and Cholsey	Side of Down Main	Earthworks between 47¼ and 47½ m.p.
Moreton Cutting and Cholsey	Up Relief	08 00 to 15 30. Trackwork between 51¼ and 51m.p.
Didcot and Challow	All	07 30 to 18 00. Earthwork and cablework between 53 and 64 m.p.
Uffington and Swindon	Side of Down and Up	07 30 to 18 30. Bridgework at 75m. 8chs. Scaffolding in use.

**SECTION B – TEMPORARY ENGINEERING WORKS – continued**

At or between	Lines affected	Remarks
<b>WESTERN REGION – continued</b>		
<b>ACTON WELLS JN. TO SWINDON – continued</b>		
<b>SATURDAY 21 JULY</b>		
Southall East and Dolphin Jn.	Down and Up Relief <b>BLOCKED</b>	01 00 to 05 45. Trackwork between 12 and 12¼m.p. <b>Trains to travel on Main lines. Down and Up Relief available Southall (E) to Hayes.</b>
<b>SATURDAY 21 to SUNDAY 22 JULY</b>		
Acton Yard	No.2 Yard <b>BLOCKED</b>	07 00 Sat to 17 00 Sun. Trackwork between 4¼ and 4½m.p.
Slough (West) and Twyford (West)	Down and Up Main <b>BLOCKED</b>	22 45 Sat to 16 30 Sun. S and T work and trackwork between 19½ and 23m.p. <b>Trains to travel on Relief lines.</b> On track machines in use.
<b>SUNDAY 22 JULY</b>		
Paddington (Acton Wells Jn.) and Maidenhead/Reading/Didcot	All	08 00 to 16 00. S and T work.
Longfield Jn. and Dolphin Jn.	Down Main <b>BLOCKED</b>	) 02 00 to 07 30. Building work between 9¼ and 10¼m.p. <b>Trains to travel on Relief lines.</b> ) <b>Movements available at Southall (East) between Down and Up Relief and Down and Up Avoiding lines.</b> Crane in use.
Dolphin Jn. and Acton (West)	Up Main <b>BLOCKED</b>	
Reading (West Jn.) and Moreton Cutting	Down and Up Main <b>BLOCKED</b>	
Scours Lane Jn. and Didcot (East)	Down and Up Relief <b>BLOCKED</b>	) 02 45 to 04 00. Overhead line work at 49m. 3chs. ) )
Scours Lane Jn. and Didcot (East)	Down and Up Relief <b>BLOCKED</b>	06 00 to 16 00. Trackwork between 51¼ and 51½m.p. <b>Trains to travel on Main lines.</b>
Foxhall Jn. and Wantage Road	Down <b>BLOCKED</b> Up <b>BLOCKED</b>	02 45 to 08 00 ) Trackwork between 02 10 to 08 00 ) 56¼ and 60¼m.p. )
<b>SUNDAY 22 to MONDAY 23 JULY</b>		
Slough (West) and Twyford (West)	Down and Up Main <b>BLOCKED</b>	23 30 Sun to 06 30 Mon. Trackwork between 22½ and 23m.p. <b>Trains to travel on Relief lines.</b> On track machines in use.
<b>TUESDAY 24 JULY</b>		
Slough (West) and Twyford (West)	Down and Up Main <b>BLOCKED</b>	01 00 to 06 30. Trackwork between 22½ and 23m.p. <b>Trains to travel on Relief lines.</b> On track machines in use.

**SECTION B – TEMPORARY ENGINEERING WORKS – continued**

<b>At or between</b>	<b>Lines affected</b>	<b>Remarks</b>
<b>WESTERN REGION – continued</b>		
<b>READING TO THEALE</b>		
<b>UNTIL FURTHER NOTICE</b>		
Reading and Heywood Road	Down and Up	S & T work.
Theale Station	Down and Up Platform	08 00 to 16 00. Platform work between 41m. 19chs. and 41m. 27chs.
<b>MONDAY 23 to FRIDAY 27 JULY</b>		
Reading (Panel)	All	08 00 to 16 00 daily. S. and T. work.

**SIGNALLING AND PERMANENT WAY ALTERATIONS****\*\***

**\*** *Items marked thus will not appear in future issues and a note must be taken of them by all concerned.*

**SOUTHERN REGION****DETAILS OF WORK ALREADY CARRIED OUT****BETWEEN WESTON AND WALLERS ASH**

Catch Points have been abolished in Up line at 60m. 52chs. (657 yards to ZW129/131 signals).  
(New Item) (32)

**LONDON MIDLAND REGION****DETAILS OF WORK REFERRED TO IN SECTION B****MONDAY 23 JULY – BLETCHLEY**

Lambs Sidings ground frame will be taken out of use and the associated trailing connection in the Down Fast line will be secured out of use, pending removal.  
(32)

**DETAILS OF WORK ALREADY CARRIED OUT****\*\* HEMEL HEMPSTEAD SOUTH JUNCTION**

The fixed diamond in the Down Slow line of the facing connection from the Up Slow to the Up Fast line has been converted to a switch diamond.  
(29)

**WESTERN REGION****DETAILS OF WORK ALREADY CARRIED OUT****AT SWINDON (RODBOURNE)**

Rodbourne 'A' Ground Frame has been temporarily removed. Points 3 and 4 have been spiked, clipped and padlocked in the normal position.

Routes 52B, 57A, 217 and 272 have been temporarily taken out of use.  
(30)

**\*\* AT RUSCOMBE JN.**

Existing Signal DM28 now has the capacity to display a flashing yellow aspect and existing Signal DM27 now has the capacity to display a flashing double yellow aspect for movements to the Down Relief line.  
(29)

---

GENERAL INSTRUCTIONS AND NOTICES

\*\* Items marked thus will not appear in future issues and a note must be taken of them by all concerned.

★ Denotes new or amended item

MISCELLANEOUS NOTICE

RULE BOOK AMENDMENTS – SD22D, 2-6-79 – 3-8-79

Please add stars to the amendments to the Rule Book on page SD5 of SD22D to indicate that these are new items published for the first time.

INSTRUCTIONS AFFECTING EASTERN REGION TRAINMEN WHEN WORKING ACROSS LONDON INTO THE LONDON MIDLAND REGION, SOUTHERN REGION AND WESTERN REGION – BR.30058

PART I – LONDON MIDLAND REGION

TABLE 'A'

Description of Block Signalling on Main Lines Absolute Block unless otherwise shown.	Stations and Signal Boxes	Distance between signal boxes		Running lines		Loops and Refuge Sidings		Permanent speed restrictions m.p.h.		Catch points, spring or unworked trailing points	
		M	Yds	Up	Down	Description	Stand-age Wag- ons L.&V.	Down	Up	Position	Gradient (Rising unless otherwise shown) 1 in

★ Page 19 HARRINGAY PARK JN. ER TO BRENT JN.  
Add:—Carlton Road Jn.

10 Through junction to Kentish Town line. (31D)

40 Fast and local lines from Finchley Road to Cricklewood Junction (applicable to Class 4, 6, 7, 8 and 9 freight trains only).

65 65 Fast lines through junction.

40 Fast to local.

50 Local to Fast.

40 40 Local lines through station.

25 Fast to Slow.

25 Slow to Fast.

25 Local to carriage loop.


25 Carriage loop to local.

20 Slow to Fast or local.

20 Fast to local.

20 Local to Fast or Goods.

20 20 To and from Depot line.

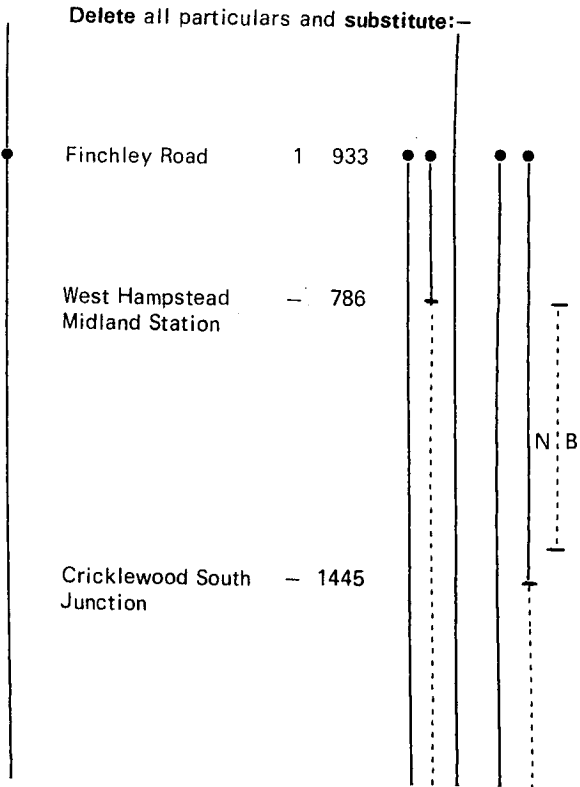

## SECTION D – GENERAL INSTRUCTIONS AND NOTICES – continued

## INSTRUCTIONS AFFECTING EASTERN REGION TRAINMEN WHEN WORKING ACROSS LONDON INTO THE LONDON MIDLAND REGION, SOUTHERN REGION AND WESTERN REGION – BR.30058 – continued

## PART I – LONDON MIDLAND REGION – continued

TABLE A – continued

Description of Block Signalling on Main Lines Absolute Block unless otherwise shown.	Stations and Signal Boxes	Distance between signal boxes		Running lines		Loops and Refuge Sidings		Permanent speed restrictions m.p.h.		Catch points, spring or unworked trailing points	
		M	Yds	Up	Down	Description	Stand-age Wag- ons L.&V.	D o w n	U p	Position	Gradient (Rising unless otherwise shown) 1 in

Page 19 – substitute – continued

●	Cricklewood Junction (Station)	–	760	●	●	U & D 61 GL No.1		25	25	Local lines between Cricklewood Station and Cricklewood Junction box.	
						U & D 61 GL No.2			40	Fast and local lines from Cricklewood Junction to Finchley Road (applicable to Class 4, 6, 7, 8 and 9 freight trains only).	
									20	Through junction to Acton Wells Jn. line.	
●	Brent Junction (See page 20 for Dudding Hill Jn. line)	–	1421	●	●				15	Through junction to Dudding Hill Jn. line.	

Amend:—  
References to Brent Jn No.2  
to read Brent Junction

(31D)

TABLE F1 – PROPELLING TRAINS OR VEHICLES

From	To	Lines	Number of vehicles and special conditions
------	----	-------	---

HARRINGAY PARK JN. TO BRENT JN.

Page 26– Amend:—

Brent Junction No.2 to read Brent Junction.

(31D)

## LOCAL INSTRUCTIONS

## HARRINGAY PARK JN. TO BRENT JN.

Page 42 – Cricklewood – Add as new second paragraph – Propelling Cricklewood Jn.

The clearing of the signal will be the Driver's authority to commence the setting back movement to Carriage Shed No.1 or No.2 arrival line and the provision of Rule Book, Section J clause 4.1 are exempt. The setting back movement must be made at walking pace and the Driver must be prepared to act on a hand signal from the Guard or Shunter when he comes into view.

(31D)

## SECTION D – GENERAL INSTRUCTIONS AND NOTICES – continued

INSTRUCTIONS AFFECTING EASTERN REGION TRAINMEN WHEN WORKING ACROSS LONDON INTO THE LONDON MIDLAND REGION, SOUTHERN REGION AND WESTERN REGION –BR.30058 – continued

## MISCELLANEOUS NOTICES

## SPEED RESTRICTION: 16 TON MINERAL WAGONS

On the Up and Down Slow lines between Hanslope and Euston all trains conveying 16 ton mineral wagons loaded or empty are limited to a maximum speed of 35m.p.h. (31D)

## PART II – SOUTHERN REGION

TABLE 'A'

Description of Block Signalling on Main Lines Absolute Block unless otherwise shown.	Stations and Signal Boxes	Distance between signal boxes		Running lines		Loops and Refuge Sidings		Permanent speed restrictions m.p.h.		Catch points, spring or unworked trailing points	
		M	Yds	Up	Down	Description	Stand-age Wag-ons L.&V.	Down	Up	Position	Gradient (Rising unless otherwise shown) 1 in

## Page 52 LATCHMERE JN. TO GLOUCESTER ROAD JN. VIA STREATHAM COMMON

Balham (DC) – Delete first permanent speed restriction and substitute:–

50 Through junction.

50 Through, Through junction and station. (31D)

## Page 73 (Page 170 Supp. Oper. Insts.)

TABLE W – B.R. AUTOMATIC WARNING SYSTEM OF TRAIN CONTROL

From	To	Lines	Remarks
LATCHMERE JUNCTION TO HITHER GREEN (VIA NUNHEAD)			
Delete entries and substitute:–			
Nunhead	Grove Park	All	– (31D)

**SECTION D – GENERAL INSTRUCTIONS AND NOTICES – continued**

**INSTRUCTIONS AFFECTING EASTERN REGION TRAINMEN WHEN WORKING ACROSS LONDON INTO THE LONDON MIDLAND REGION, SOUTHERN REGION AND WESTERN REGION – BR.30058 – continued**

**PART II – SOUTHERN REGION – continued**

**LOCAL INSTRUCTIONS**

**Pages 83/84 (Pages 178/9 Supp. Oper. Insts.)**

**MILLBROOK – SOUTHAMPTON MARITIME FREIGHTLINER TERMINAL**

**Engineer's Sidings Nos.1 and 2 and Cripple Siding – Amend heading to read:–  
"Engineer's sidings Nos.1 and 2"**

**Delete "also the cripple siding" from the first line.**

**Add as new instruction:–**

**Maritime New Holding Siding and Cripple Siding**

All movements between these sidings and the Engine Line must be attended by the Senior Railman, who will authorise the entry to either siding on receipt of permission from the terminal overseer. The terminal overseer will authorise all movements from the sidings as far as the "Stop" Board at the convergence of the New Holding Siding and Engine Line. The Senior Railman will be responsible for the operation of the Engine Line hand points and for their restoration to the normal Engine Line position after the movement has been completed and must also assist in controlling movements into the sidings.

The points to the Cripple Siding must be clipped and padlocked towards the New Holding Siding position when not being used. The padlock key must be kept in the Maritime Freightliner Traffic Office under the control of the terminal overseer. (31D)

---

**MISCELLANEOUS NOTICE**

**SPEED RESTRICTIONS : TANK WAGONS ETC., 15 FT. WHEEL BASE OR LESS**

The speed of certain 2-axle rail tanks with a wheel base of 15ft. or less, and PRESFLO, CEMFLO and R.I.V. types when running in the empty/discharged condition must be restricted to a maximum speed at 45 m.p.h.

T.O.P.S. train lists show the applicable speed, and every effort should be made to provide guards with a valid train list.

If no train list is available, and any doubt exists, 45m.p.h. restriction must be applied, or where a lower speed than 45 m.p.h. is in operations this must apply. (OD15/Pad 6/TV)

(31D)

---

MO/45/S

YORK

G. GRAHAM  
CHIEF OPERATING MANAGER

17 JULY, 1979

*Receipt of this notice need not be acknowledged. If the "S" Notice is not received by the normal time, advise your Supervisor.*
